



**Verified Carbon
Standard**

RENEWABLE SOLAR POWER PROJECT BY RENEW SOLAR POWER PRIVATE LIMITED

ReNew

Document Prepared by ReNew Power Private Limited

Project Title	Renewable Solar Power Project by ReNew Solar Power Private Limited
Version	2.0
Report ID	1851
Date of Issue	20-September -2023
Project ID	1851
Monitoring Period	01-January-2023 to 31-March-2023
Prepared By	Gaurav Kumar Singh Assistant Manager -Carbon Business ReNew Power Private Limited
Contact	ReNew Power Private Limited, ReNew.Hub, Commercial Block-1, Zone-6, Golf Course Road, DLF City, Phase V, Gurugram, Haryana 122009 Website: www.renewpower.in Email ID: carbon.registry@renewpower.in

CONTENTS

1	PROJECT DETAILS.....	3
1.1	Summary Description of the Implementation Status of the Project	3
1.2	Sectoral Scope and Project Type	4
1.3	Project Proponent	4
1.4	Other Entities Involved in the Project	5
1.5	Project Start Date	5
1.6	Project Crediting Period	5
1.7	Project Location	5
1.8	Title and Reference of Methodology	11
1.9	Participation under other GHG Programs.....	11
1.10	Other Forms of Credit and Supply Chain (Scope 3) Emissions	11
1.11	Sustainable Development Contributions	11
2	SAFEGUARDS.....	14
2.1	No Net Harm	14
2.2	Local Stakeholder Consultation	14
2.3	AFOLU-Specific Safeguards	14
3	IMPLEMENTATION STATUS	14
3.1	Implementation Status of the Project Activity	14
3.2	Deviations	26
3.3	Grouped Projects	27
4	DATA AND PARAMETERS.....	27
4.1	Data and Parameters Available at Validation	27
4.2	Data and Parameters Monitored.....	28
4.3	Monitoring Plan.....	33
5	QUANTIFICATION OF GHG EMISSION REDUCTIONS AND REMOVALS	37
5.1	Baseline Emissions	37
5.2	Project Emissions	38
5.3	Leakage.....	38
5.4	Net GHG Emission Reductions and Removals.....	38
	APPENDIX I: <METER CALIBRATION DETAILS>	41

1 PROJECT DETAILS

1.1 Summary Description of the Implementation Status of the Project

The main purpose of this project activity is to generate clean form of electricity through renewable solar energy sources. The project activity involves total capacity of 927 MW solar power project which are installed in Gujarat, Karnataka, Madhya Pradesh, Rajasthan and Telangana states of India. The solar projects have been developed by the SPVs of ReNew Solar Power Private Limited.

All the SPVs are of ReNew Solar Power Private Limited. The project is promoted by ReNew Solar Power Private Limited.

Total emission reductions achieved in this monitoring period:

During the Current Monitoring Period from 01-January-2023 to 31-March-2023 (First and last date included) the project activity has supplied 516,308.01 MWh of electricity, and thus contributing to the GHG reductions 489,201 tCO₂e (Round down value).

The project started operation from 13-February-2017 and it is still in running condition. In current monitoring period, no major breakdown/shutdown of plant happened which could have had an impact on emission reduction.

Audit Type	Period	Program	VVB Name	Number of years
Validation/ Verification	13-February-2017 – 25-October-2018	VCS	IGAI Technologic al Center, S.A. (Applus+ Certification)	2 years 8 months
Verification	26-October-2018 – 24-December-2019	VCS	Earthood Services Private Limited	1 years 2 months
Verification	25-December-2019 – 25-May-2021	VCS	TÜV SÜD South Asia Pvt. Ltd	1 year 5 months
Verification	26-May-2021 – 31-	VCS	IGAI Technologic al Center,	7 months

	December-2021		S.A.(Applus+ Certification)	
Verification	01-January-2022 – 30-June-2022	VCS	LGA Technological Center, S.A.(Applus+ Certification)	6 months
Verification	01-July-2022 – 31-December-2022	VCS	Earthood Services Private Limited	6 months
Verification	01-January-2023 – 31-March-2023	VCS	Earthood Services Private Limited	3 months
Total	13-February-2017 – 31-March-2023			6 years 01 month

1.2 Sectoral Scope and Project Type

The project activity falls under the following Sectoral scope and Project Type:

Sectoral Scope: 01 - Energy industries (renewable / non-renewable sources)

Project Type: I - Renewable Energy Projects

Project Category: Grid-connected electricity generation from renewable sources
ACM0002-Version 19.0¹

Tools referred with above methodology and applicable for project activity are:

- Tool to calculate the emission factor for an electricity system²- Version 07.0 (EB 100, Annex 04)
- Methodological Tool- Tool for the demonstration and assessment of additionality³- Version 07.0.0 (EB 70, Annex 08).

1.3 Project Proponent

Organization name	Renew Solar Power Private Limited
Contact person	Mr. Aditya Sharma

¹ <http://cdm.unfccc.int/methodologies/DB/VJI9AX539D9MLOPXN2AY9UR1N4IYGD>

² <http://cdm.unfccc.int/methodologies/PAmethodologies/tools/am-tool-07-v7.0.pdf>

³ <http://cdm.unfccc.int/methodologies/PAmethodologies/tools/am-tool-01-v7.0.0.pdf>

Title	PP Representative
Address	ReNew Hub, Commercial Block-1, Zone 6, Golf Course Road, DLF City, Phase-V, Gurugram- 122009, Haryana
Telephone	+91-8800915324
Email	Aditya.Sharma@renewpower.in

1.4 Other Entities Involved in the Project

Organization name	NA
Role in the Project	NA
Contact person	NA
Title	NA
Address	NA
Telephone	NA
Email	NA

1.5 Project Start Date

Start date of the project activity is the earliest date of interconnection with the grid i.e.13-February-2017 which is the date of commissioning of 24 MW solar project activity by Renew Mega Solar Power Private Limited.

1.6 Project Crediting Period

Crediting Period Start date: 13-February-2017

Crediting Period End date: 12-February-2027

The project activity adopts renewable crediting period of 10 years period which can be renewed for maximum 2 times.

1.7 Project Location

The details of the project locations are mentioned in the table below.

Name of SPVs	Capacity (MW)	Village(s)	Tehsil / Mandal	District	State
Bhumi Prakash Private Limited	20 MW	Hirebudur	Deodurga	Raichur	Karnataka


Renew Wind Energy (MP Four) Private Limited	20 MW	Chincholi	Chincholi	Kalaburagi	
Renew Agni Power Private Limited	20 MW	Upparhosahalli	Siruguppa	Ballari	
Renew Wind Energy (Karnataka 3) Private Limited	20 MW	Ladha	Bhalki	Bidar	
Tarun Kiran Bhoomi Private Limited	20 MW	Gola (B)	Aland	Kalaburagi	
Renew Wind Energy (Karnataka 4) Private Limited	20 MW	Nirna	Humnabad	Bidar	
Renew Wind Energy (Budh 3) Private Limited	20 MW	Santhpur near Eklara	Aurad	Bidar	
Renew Wind Energy (Budh 3) Private Limited	20 MW	Nirna	Humnabad	Bidar	
Renew Wind Energy (Budh 3) Private Limited	20 MW	Wadagere & Aikur	Shahapur	Yadagir	
Renew Wind Energy (Maharashtra) Private Limited	20 MW	Saidapur & Malhar	Yadagir	Yadagir	
Renew Wind Energy (Rajasthan Four) Private Limited	20 MW	Gundikaval	Turuvekere	Tumkur	
Renew Wind Energy (MP Three) Private Limited	20 MW	Kattige	Honnali	Davangere	
Renew Saur Urja Private Limited	50 MW	Thalekhan	Lingasugur		
Renew Wind Energy (TN2) Private Limited	50 MW	Thirumani, Rayacherlu, Vallur, Balasamudra, Kyataganacherlu	NagalamadikeH obli, Pavagada	Tumkur	Gujarat
Renew Solar Energy (Karnataka Two) Private Limited	40 MW	Charanka	Santalpur	Patan	
Renew Clean Energy Private Limited	51 MW	Bhensarwas	Shadora	Ashok Nagar	
Aalok Solarfarms Limited	10 MW	Badisid	Bap	Jodhpur	
Abha Solarfarms Limited	10 MW	Badisid	Bap	Jodhpur	Rajasthan

Heramba Renewables Limited	20 MW	Hanawat Nagar	Bap	Jodhpur	
Shreyas Solarfarms Limited	20 MW	Khetusar Nagar	Bap	Jodhpur	
ReNew Solar Energy (Telangana) Private Limited	143 MW	Dharamaraopet & Kankal	Sadasivanagar	Nizamabad	Telangana
Renew Mega Solar Power Pvt Limited	48 MW	Andugulapet	Mandamarri	Adilabad	
Renew Saur Shakti Private Limited	30 MW	Vangara	Bheemdevarapally	Karimnagar	
Renew Saur Shakti Private Limited	65 MW	Minpur	-	Medak	
Renew Wind Energy (TN2) Private Limited	100 MW	Gudibanda	Addakal	Mahabubnagar	
Prathamesh Solarfarms Limited	50 MW	Dodaguntapally	Peddmandadi	Mahabubnagar	

The Geo-coordinates of the project site is mentioned below:

Name of SPVs	Capacity (MW)	Latitude	Longitude
Bhumi Prakash Private Limited	20 MW	16.3° N	76.8° E
Renew Wind Energy (MP Four) Private Limited	20 MW	17.4° N	77.4° E
Renew Agni Power Private Limited	20 MW	15.5° N	76.9° E
Renew Wind Energy (Karnataka 3) Private Limited	20 MW	18° 0'5.81"N	77°18'32.57"E
Tarun Kiran Bhoomi Private Limited	20 MW	17.4° N	76.7° E
Renew Wind Energy (Karnataka 4) Private Limited	20 MW	17.7° N	77.3° E
Renew Wind Energy (Budh 3) Private Limited	20 MW	18°11'47.91"N	77°26'46.34"E
Renew Wind Energy (Budh 3) Private Limited	20 MW	17.75° N	77.35° E
Renew Wind Energy (Budh 3) Private Limited	20 MW	16.6° N	77.0°E
Renew Wind Energy (Maharashtra) Private Limited	20 MW	16.6° N	77.3°E
Renew Wind Energy (Rajasthan Four) Private Limited	20 MW	13.2°N	76.8°E
Renew Wind Energy (MP Three) Private Limited	20 MW	14.3° N	75.6° E
Renew Saur Urja Private Limited	50 MW	15°53'53" N	76°33'26" E
Renew Wind Energy (TN2) Private Limited	50 MW	14.237 N	77.486 E
Renew Solar Energy (Karnataka Two) Private Limited	40 MW	23°54'56.45" N	71°12'4.79" E
Renew Clean Energy Private Limited	51 MW	24.03117°N	76.667943°E
Aalok Solarfarms Limited	10 MW	27.4° N	72.4° E
Abha Solarfarms Limited	10 MW	27.4° N	72.4° E
Heramba Renewables Limited	20 MW	27.4° N	72.1° E
Shreyas Solarfarms Limited	20 MW	27.3° N	71.9° E

ReNew Solar Energy (Telangana) Private Limited	143 MW	N 18.6°	E 78.3°
Renew Mega Solar Power Pvt Limited	48 MW	N 18.985290°	E 79.446397°
Renew Saur Shakti Private Limited	30 MW	18.1° N	79.4° E
Renew Saur Shakti Private Limited	65 MW	17° 57.951' N	78° 03.968' E
Renew Wind Energy (TN2) Private Limited	100 MW	16.6°N	77.9°E
Prathamesh Solarfarms Limited	50 MW	16°25'12" N	78°4'40.80" E

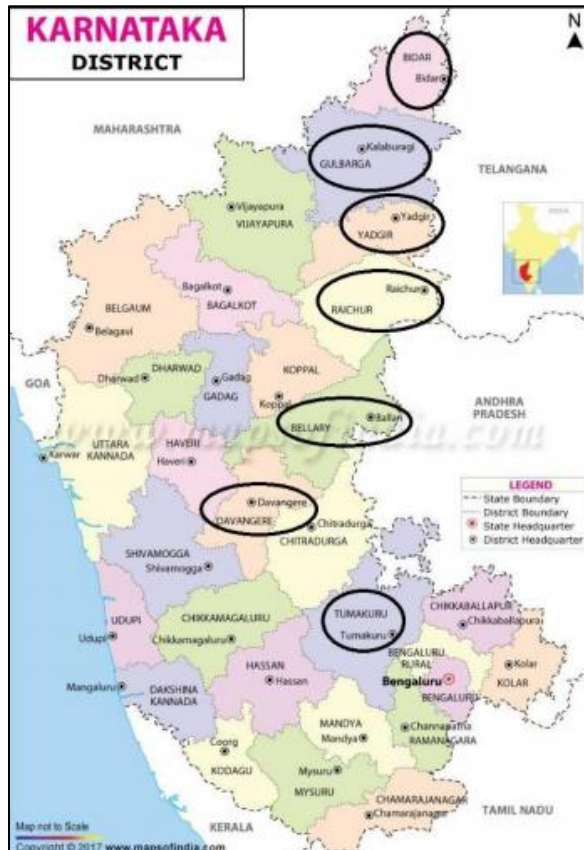


Gujarat Site:



Rajasthan Site:



Madhya Pradesh Site:

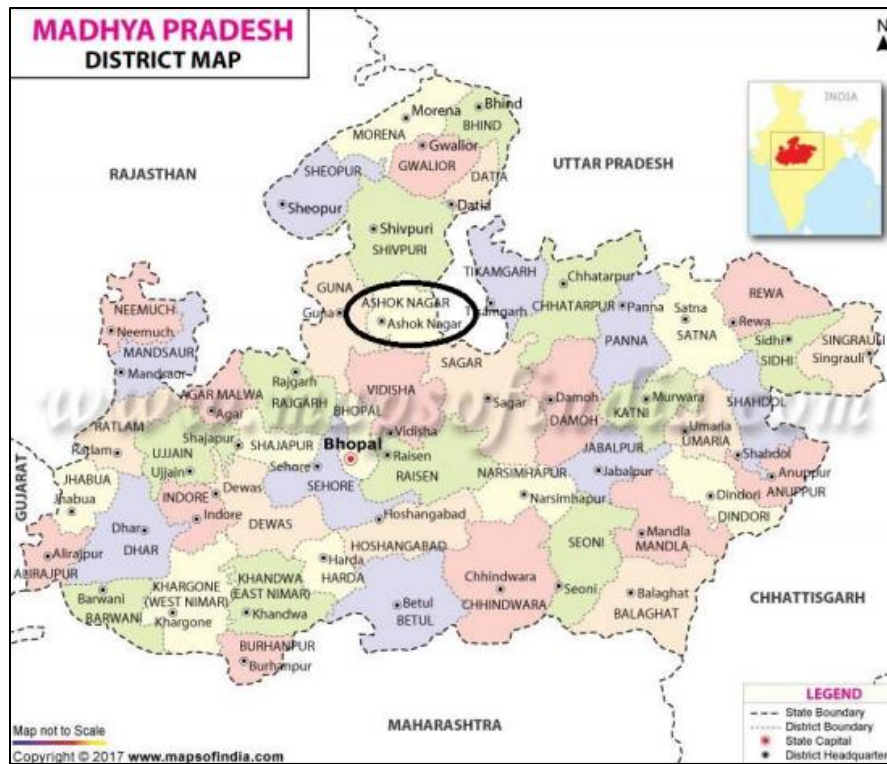

Telangana Site:



1.8 Title and Reference of Methodology

Title: Grid-connected electricity generation from renewable sources

Reference: The project activity meets the eligibility criteria of large-scale project as it is more than 15 MW

Methodology: ACM0002: Grid-connected electricity generation from renewable sources⁴ - Version 19.0

Type I: Energy industries (renewable / non-renewable sources)

Category: Approved Consolidated Methodology (ACM0002)

Tools referred with above methodology and applicable for project activity are:

- Tool to calculate the emission factor for an electricity system⁵- Version 07.0 (EB 100, Annex 04)
- Methodological Tool- Tool for the demonstration and assessment of additionality⁶- Version 07.0.0 (EB 70, Annex 08).

1.9 Participation under other GHG Programs

The project has neither been registered nor seeking registration under any other GHG programs. The project is registered only in VCS program.

1.10 Other Forms of Credit and Supply Chain (Scope 3) Emissions

Emission Trading Programs and Other Binding Limits:

Net GHG emission reductions or removals generated by the project are not being used for compliance with an emissions trading program or to meet binding limits on GHG emissions in any Emission Trading program or other binding limits.

Other Forms of Environmental Credit:

Not applicable, as the project is not registered in any other GHG mechanism other than VCS. Also, the project activity is not availing any REC benefits and the same can be confirmed from publicly available link of REC generators.

Web-link:

https://www.recregistryindia.nic.in/index.php/general/publics/registered_regens

1.11 Sustainable Development Contributions

Contribution to sustainable development:

Ministry of Environment, Forest and Climate Change, has stipulated economic, social, environment and technological well-being as the four indicators of

⁴ <http://cdm.unfccc.int/methodologies/DB/VJI9AX539D9MLOPXN2AY9UR1N4IYGD>

⁵ <http://cdm.unfccc.int/methodologies/PAmethodologies/tools/am-tool-07-v7.0.pdf>

⁶ <http://cdm.unfccc.int/methodologies/PAmethodologies/tools/am-tool-01-v7.0.0.pdf>

sustainable development. The project contributes to sustainable development using the following ways.

Social well-being: The project helps in generating employment opportunities during the construction and operation phases. The project activity leads to development in infrastructure in the region like development of roads and also may promote business with improved power generation.

Economic well-being: The project is a clean technology investment in the region, which would not have taken place in the absence of the VCS benefits. The project activity helps to reduce the demand supply gap in the state.

Technological well-being: The successful operation of project activity leads to promotion of solar power generation and encourages other entrepreneurs to participate in similar projects

Environmental well-being: Solar being a renewable source of energy, it reduces the dependence on fossil fuels and conserves natural resources which are on the verge of depletion. Due to its zero emission the Project activity also helps in avoiding significant amount of GHG emission.

Table 1: Sustainable Development Contributions

Row number	SDG Target	SDG Indicator	Net Impact on SDG Indicator	Current Project Contributions	Contributions Over Project Lifetime
Sequential row number	SDG Target number	Number and text of SDG indicator or, if no official SDG indicator is applicable, user-defined indicator	Indicate the project's contribution to the SDG Indicator (implemented activities to increase or decrease)	Brief description of the quantifiable impact of the project's activities related to the SDG indicator, during the monitoring period.	Brief description of the cumulative quantifiable impact of the project's activities related to the SDG indicator, over the project lifetime.
1)					
2)					
3)					
4)					

This is not applicable up to 2025.

2 SAFEGUARDS

2.1 No Net Harm

The project activity does not involve any major construction activity. It primarily requires the installation of the solar PV panels, interfacing the generators with the State Electricity Board by setting up HT transmission lines and installation of other accessories.

The report on "Developmental Impacts and Sustainable Governance Aspects of Renewable Energy Projects" prepared by MNRE dated September 2013. This report clearly mentioned that solar PV project activity operations do not result in direct air pollution, noise pollution. Please refer below web link for the same⁷.

Thus, there are no any significant impacts due to implementation of project activity on air, water, soil quality and ambience are envisaged due to the project activity. Also, there are no negative environmental and socio-economic impacts due to implementation of the project activity as this is a renewable solar project.

2.2 Local Stakeholder Consultation

The local stakeholder meeting was carried out for the project activity and the details of the same can be referred from the registered VCS PD.

As a part of continuous feedback from stakeholders, the PP also placed a grievance register onsite wherein the stakeholders can put down their complaints and the same, if found genuine, are addressed immediately. However, during the current monitoring period, no comments or feedbacks were received.

2.3 AFOLU-Specific Safeguards

Not Applicable, as this is not an AFOLU project.

3 IMPLEMENTATION STATUS

3.1 Implementation Status of the Project Activity

The project activity involves the installation of solar project. The total installed capacity of the project is 927 MW Solar project located at Gujarat, Karnataka, Madhya Pradesh, Rajasthan and Telangana states in India. The project is promoted by ReNew Solar Power Private Limited.

⁷ <http://mnre.gov.in/file-manager/UserFiles/report-on-developmental-impacts-of-RE.pdf>

The Project activity is a new facility (Greenfield) and the electricity generated by the project is exported to the Indian electricity grid. The project therefore displaces an equivalent amount of electricity which would have otherwise been generated by fossil fuel dominant electricity grid.

During the Current Monitoring Period, all the solar plants were operational and the project activity has supplied 516,308.01 MWh of electricity, and thus contributing to the GHG reductions 489,201 tCO₂e (Round down value).

The technical details of the project activity are provided below.

The technical specification for 20 MW solar project by Bhumi Prakash Private Limited at Karnataka.

Sl. No.	Technical details of the equipment ⁸	Description
1	Modules capacity and No. of Module	Model capacity- 320 Wp, 325 Wp No. of Modules- 21, 21
2	Number of Inverters & Capacity	20 Inverters Capacity- 1 MW
3	Number of Transformers & Capacity	5 transformers of 4 MVA 1 transformer of 15/20 MVA

The technical specification for 20 MW solar project by Renew Wind Energy (MP Four) Private Limited at Karnataka.

Sl. No.	Technical details of the equipment ⁹	Description
1	Modules capacity and No. of Module	Model capacity- 320 Wp No. of Modules- 21
2	Number of Inverters & Capacity	20 Inverters Capacity- 1 MW
3	Number of Transformers & Capacity	5 transformers of 4 MVA 1 transformer of 16/20 MVA

The technical specification for 20 MW solar project by Renew Agni Power Private Limited at Karnataka.

Sl. No.	Technical details of the equipment ¹⁰	Description
---------	--	-------------

⁸ It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 20 MW.

⁹ It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 20 MW.

¹⁰ It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 20 MW.

1	Modules capacity and No. of Module	Model capacity- 315 Wp, 320 Wp & 325 Wp No. of Modules- 21,21,21
2	Number of Inverters & Capacity	465 Inverters Capacity- 0.043 MW
3	Number of Transformers & Capacity	5 transformers of 4 MVA 1 transformer of 16/20 MVA

The technical specification for 20 MW solar project by Renew Wind Energy (Karnataka 3) Private Limited at Karnataka.

Sl. No.	Technical details of the equipment ¹¹	Description
1	Modules capacity and No. of Module	Model capacity- 315 Wp, 320 Wp & 325 Wp No. of Modules- 21,21,21
2	Number of Inverters & Capacity	20 Inverters Capacity- 1 MW
3	Number of Transformers & Capacity	5 transformers of 4 MVA 1 transformer of 16/20 MVA

The technical specification for 20 MW solar project by Tarun Kiran Bhoomi Private Limited at Karnataka.

Sl. No.	Technical details of the equipment ¹²	Description
1	Modules capacity and No. of Module	Model capacity- 315 Wp, 320 Wp No. of Modules- 21,21
2	Number of Inverters & Capacity	8 Inverters Capacity- 2.5 MW
3	Number of Transformers & Capacity	4 transformers of 4 MVA 1 transformer of 16/20 MVA

The technical specification for 20 MW solar project by Renew Wind Energy (Karnataka 4) Private Limited at Karnataka.

¹¹ It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 20 MW.

¹² It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 20 MW.

Sl. No.	Technical details of the equipment ¹³	Description
1	Modules capacity and No. of Module	Model capacity- 315 Wp, 320 Wp & 325 Wp No. of Modules- 20,20,20
2	Number of Inverters & Capacity	20 Inverters Capacity- 1 MW
3	Number of Transformers & Capacity	5 transformers of 4 MVA 1 transformer of 16/20 MVA

The technical specification for 20 MW solar project by Renew Wind Energy (Budh 3) Private Limited at Eklara site in Karnataka.

Sl. No.	Technical details of the equipment ¹⁴	Description
1	Modules capacity and No. of Module	Model capacity- 320 Wp, 325 Wp & 330 Wp No. of Modules- 20,20,20
2	Number of Inverters & Capacity	8 Inverters Capacity- 2.52 MW
3	Number of Transformers & Capacity	5 transformers of 4 MVA 1 transformer of 16/20 MVA

The technical specification for 20 MW solar project by Renew Wind Energy (Budh 3) Private Limited at Nirna site in Karnataka.

Sl. No.	Technical details of the equipment ¹⁵	Description
1	Modules capacity and No. of Module	Model capacity- 325 Wp & 330 Wp No. of Modules- 20,20
2	Number of Inverters & Capacity	8 Inverters Capacity- 2.52 MW

¹³ It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 20 MW.

¹⁴ It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 20 MW.

¹⁵ It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 20 MW.

3	Number of Transformers & Capacity	4 transformers of 5 MVA 1 transformer of 15/20 MVA
---	-----------------------------------	---

The technical specification for 20 MW solar project by Renew Wind Energy (Budh 3) Private Limited at Wadagere site in Karnataka.

Sl. No.	Technical details of the equipment ¹⁶	Description
1	Modules capacity and No. of Module	Model capacity- 320 Wp, 325 Wp & 330 Wp No. of Modules- 20,20,20
2	Number of Inverters & Capacity	30 Inverters Capacity- 0.68 MW
3	Number of Transformers & Capacity	4 transformers of 5 MVA 1 transformer of 15/20 MVA

The technical specification for 20 MW solar project by Renew Wind Energy (Maharashtra) Private Limited at Karnataka

Sl. No.	Technical details of the equipment ¹⁷	Description
1	Modules capacity and No. of Module	Model capacity- 315 Wp, 320 Wp & 325Wp No. of Modules- 21,21,21
2	Number of Inverters & Capacity	30 Inverters Capacity- 0.68 MW
3	Number of Transformers & Capacity	5 transformers of 4 MVA 1 transformer of 15/20 MVA

The technical specification for 20 MW solar project by Renew Wind Energy (Rajasthan Four) Private Limited at Karnataka.

Sl. No.	Technical details of the equipment ¹⁸	Description
---------	--	-------------

¹⁶ It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 20 MW.

¹⁷ It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 20 MW.

¹⁸ It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 20 MW.

1	Modules capacity and No. of Module	Model capacity- 320 Wp& 325Wp No. of Modules- 21,21
2	Number of Inverters & Capacity	20 Inverters Capacity- 1 MW
3	Number of Transformers & Capacity	5 transformers of 4 MVA 1 transformer of 16/20 MVA

The technical specification for 20 MW solar project by Renew Wind Energy (MP Three) Private Limited at Karnataka.

Sl. No.	Technical details of the equipment ¹⁹	Description
1	Modules capacity and No. of Module	Model capacity- 320 Wp, 325 Wp& 330Wp No. of Modules- 21,21,21
2	Number of Inverters & Capacity	20 Inverters Capacity- 1 MW
3	Number of Transformers & Capacity	5 transformers of 4 MVA 1 transformer of 15/20 MVA

The technical specification for 50 MW solar project by Renew Saur Urja Private Limited at Karnataka.

Sl. No.	Technical details of the equipment ²⁰	Description
1	Modules capacity and No. of Module	Model capacity- 315 Wp, 320 Wp& 325Wp No. of Modules- 21,42,21
2	Number of Inverters & Capacity	23 Inverters of 1 MW 24 Inverters of 1.125 MW
3	Number of Transformers & Capacity	6 transformers of 4.5 MVA 5 transformers of 4 MVA 1 transformer of 3 MVA 2 transformers of 20/25 MVA

¹⁹It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 20 MW.

²⁰It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 50 MW.

The technical specification for 50 MW solar project by Renew Wind Energy (TN2) Private Limited at Karnataka.

Sl. No.	Technical details of the equipment ²¹	Description
1	Modules capacity and No. of Module	Model capacity- 320 Wp, 325 Wp, 330 Wp, 340 Wp & 345 Wp No. of Modules- 19,21,21,21,21
2	Number of Inverters & Capacity	20 Inverters of 2.5 MW
3	Number of Transformers & Capacity	10 transformers of 5 MVA 2 transformers of 20/25 MVA

The technical specification for 40 MW solar project by Renew Solar Energy (Karnataka Two) Private Limited at Gujarat.

Sl. No.	Technical details of the equipment ²²	Description
1	Modules capacity and No. of Module	Model capacity- 315 Wp, 320 Wp & 325 Wp No. of Modules- 20,20,20
2	Number of Inverters & Capacity	40 Inverters of 1 MW
3	Number of Transformers & Capacity	10 transformers of 4 MVA 2 transformers of 16/20 MVA

The technical specification for 51 MW solar project by Renew Clean Energy Private Limited at Madhya Pradesh.

Sl. No.	Technical details of the equipment ²³	Description
1	Modules capacity and No. of Module	Model capacity- 117.5 Wp No. of Modules- 32
2	Number of Inverters & Capacity	6 Inverters of 2.5 MW 12 Inverters of 3 MW
3	Number of Transformers & Capacity	6 transformers of 6 MVA 3 transformers of 5 MVA 2 transformers of 25/30 MVA

²¹It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 50 MW.

²²It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 40 MW.

²³It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 51 MW.

The technical specification for 10 MW solar project by Aalok Solarfarms Limited at Rajasthan.

Sl. No.	Technical details of the equipment ²⁴	Description
1	Modules capacity and No. of Module	Model capacity- 315 Wp No. of Modules- 20
2	Number of Inverters & Capacity	10 Inverters of 1 MW
3	Number of Transformers & Capacity	5 transformers of 2 MVA

The technical specification for 10 MW solar project by Abha Solarfarms Limited at Rajasthan.

Sl. No.	Technical details of the equipment ²⁵	Description
1	Modules capacity and No. of Module	Model capacity- 315 Wp No. of Modules- 20
2	Number of Inverters & Capacity	10 Inverters of 1 MW
3	Number of Transformers & Capacity	5 transformers of 2 MVA

The technical specification for 20 MW solar project by Heramba Renewbles Limited at Rajasthan.

Sl. No.	Technical details of the equipment ²⁶	Description
1	Modules capacity and No. of Module	Model capacity- 315 Wp No. of Modules- 20
2	Number of Inverters & Capacity	10 Inverters of 1 MW
3	Number of Transformers & Capacity	10 transformers of 2 MVA

²⁴It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 10 MW.

²⁵It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 10 MW.

²⁶It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 10 MW.

The technical specification for 20 MW solar project by Shreyas Solarfarms Limited at Rajasthan.

Sl. No.	Technical details of the equipment ²⁷	Description
1	Modules capacity and No. of Module	Model capacity- 315 Wp No. of Modules- 20
2	Number of Inverters & Capacity	10 Inverters of 1 MW
3	Number of Transformers & Capacity	10 transformers of 2 MVA

The technical specification for 143 MW solar project by ReNew Solar Energy (Telangana) Private Limited at Telangana.

Sl. No.	Technical details of the equipment ²⁸	Description
1	Modules capacity and No. of Module	Model capacity- 310 Wp, 315 Wp, 320 Wp & 325 Wp No. of Modules- 21,21,21,21
2	Number of Inverters & Capacity	130 Inverters of 1 MW
3	Number of Transformers & Capacity	31 transformers of 4.4 MVA 3 transformers of 2.2 MVA 3 transformers of 40/50 MVA

The technical specification for 48 MW solar project by Renew Mega Solar Power Private Limited at Telangana.

Sl. No.	Technical details of the equipment ²⁹	Description
1	Modules capacity and No. of Module	Model capacity- 310 Wp, 315 Wp & 320 Wp No. of Modules- 21,21,21
2	Number of Inverters & Capacity	48 Inverters of 1 MW
3	Number of Transformers & Capacity	12 transformers of 4 MVA 2 transformers of 25/30 MVA

²⁷It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 10 MW.

²⁸It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 143 MW.

²⁹It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 48 MW.

The technical specification for 30 MW solar project by Renew Saur Shakti Private Limited at Telangana.

Sl. No.	Technical details of the equipment ³⁰	Description
1	Modules capacity and No. of Module	Model capacity- 320 Wp No. of Modules- 21
2	Number of Inverters & Capacity	30 Inverters of 1 MW
3	Number of Transformers & Capacity	7 transformers of 4 MVA 1 transformer of 2 MVA 1 transformers of 25/30 MVA

The technical specification for 65 MW solar project by Renew Saur Shakti Private Limited at Telangana.

Sl. No.	Technical details of the equipment ³¹	Description
1	Modules capacity and No. of Module	Model capacity- 315 Wp, 320 Wp & 325 Wp No. of Modules- 42,84,42
2	Number of Inverters & Capacity	65 Inverters of 1 MW
3	Number of Transformers & Capacity	16 transformers of 4 MVA 1 transformer of 1 MVA 1 transformers of 25/30 MVA 1 transformers of 40/50 MVA

The technical specification for 100 MW solar project by Renew Wind Energy (TN2) Private Limited at Telangana.

Sl. No.	Technical details of the equipment ³²	Description
1	Modules capacity and No. of Module	Model capacity- 320 Wp, 325 Wp & 330 Wp No. of Modules- 60,60,60

³⁰It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 30 MW.

³¹It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 65 MW.

³²It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 100 MW.

2	Number of Inverters & Capacity	28 Inverters of 2.5 MW 30 Inverters of 1 MW
3	Number of Transformers & Capacity	6 transformers of 4 MVA 3 transformers of 2 MVA 14 transformers of 5 MVA 2 transformers of 40/50 MVA

The technical specification for 50 MW solar project by Prathamesh Solar farms Limited at Telangana.

Sl. No.	Technical details of the equipment ³³	Description
1	Modules capacity and No. of Module	Model capacity- 320 Wp & 325 Wp No. of Modules- 20,20
2	Number of Inverters & Capacity	50 Inverters of 1 MW
3	Number of Transformers & Capacity	12 transformers of 4 MVA 2 transformers of 1 MVA

The commissioning details of this project activity is given below:

Name of SPVs ³⁴	Capacity in MW	Date of Commissioning	Connection with Grid	State	Usage
Bhumi Prakash Private Limited	20 MW	26-September-2017	Indian Grid	Karnataka	Sale to State Discom
Renew Wind Energy (MP Four) Private Limited	20 MW	28-April-2017			Sale to State Discom
Renew Agni Power Private Limited	20 MW	31-March-2017			Sale to State Discom
Renew Wind Energy (Karnataka 3) Private Limited	20 MW	27-March-2017			Sale to State Discom
Tarun Kiran Bhoomi Private Limited	20 MW	31-March-2017			Sale to State Discom
Renew Wind Energy (Karnataka 4) Private Limited	20 MW	31-March-2017			Sale to State Discom

³³It is to be noted that in future there is possibility of change in module configuration, however project capacity in total will remain same as 50 MW.

³⁴ The SPV names mentioned in the table are in accordance with their respective Commissioning Certificates.

Renew Wind Energy (Budh 3) Private Limited	20 MW	16-March-2018			Sale to 3rd Party
Renew Wind Energy (Budh 3) Private Ltd	20 MW	09-March-2018			Sale to 3rd Party
Renew Wind Energy (Budh 3) Private Limited	20 MW	30-December- 2017			Sale to 3rd Party
Renew Wind Energy (Maharashtra) Private Limited	20 MW	13-October- 2017			Sale to State Discom
Renew Wind Energy (Rajasthan Four) Private Limited	20 MW	07-December- 2017			Sale to State Discom
Renew Wind Energy (MP Three) Private Limited	20 MW	11-November- 2017			Sale to State Discom
Renew Saur Urja Private Limited	50 MW	26-May-2017			Sale to 3rd Party
Renew Wind Energy (TN2) Private Limited	50 MW	14-December- 2017			Sale to NTPC Limited
Renew Solar Energy (Karnataka Two) Private Limited	40 MW	31-March-2017		Gujarat	Sale to SECI Limited
Renew Clean Energy Private Limited	51 MW	01-October- 2017		Madhya Pradesh	Sale to State Discom
Aalok Solarfarms Limited	10 MW	06-November- 2017		Rajasthan	Sale to NTPC Limited
Abha Solarfarms Limited	10 MW	17-October- 2017			Sale to NTPC Limited
Heramba Renewbles Limited	20 MW	10 MW on 17- October-2017 10 MW on 28- October-2017			Sale to NTPC Limited

Shreyas Solarfarms Limited	20 MW	17-November-2017			Sale to NTPC Limited
ReNew Solar Energy (Telangana) Private Limited	143 MW	44 MW on 28-April-2017		Telangana	Sale to State Discom
		17.6 MW on 16-May-2017			
		44 MW on 22-June-2017			
		15.4 MW on 03-July-2017			
		22 MW on 12-July-2017			
Renew Mega Solar Power Private Limited	48 MW	24 MW on 13-February-2017			Sale to State Discom
		24 MW on 21-February-2017			
Renew Saur Shakti Private Limited	30 MW	8 MW on 14-February-2017			Sale to State Discom
		10 MW on 04-March-2017			
		6 MW on 30-March-2017			
		4.5 MW on 30-May-2017			
		1.5 Mw on 11-June-2017			
Renew Saur Shakti Private Limited	65 MW	58 MW on 29-May-2017			Sale to State Discom
		7 MW on 07-July-2017			
Renew Wind Energy (TN2) Private Limited	100 MW	01-November-2017			Sale to NTPC Limited
Prathamesh Solarfarms Limited	50 MW	20-September-2017			Sale to State Discom
Total	927 MW				

3.2 Deviations

3.2.1 Methodology Deviations

Not Applicable, as there are no methodological deviations.

3.2.2 Project Description Deviations

From January-2020 onwards, REA statements are being issued for the SPV- Renew Wind Energy (TN2) Private Limited, 50 MW Pavagada site. But the source of data for the generation data was Form-B. Hence, the generation data has been taken from the REA statements. The change in source of data for the generation is as per the requirement of State electricity authority and PP has no role to play in it. Therefore, PP applied for deviation from the source of data for generation from the registered PD.

The above-mentioned deviation was approved during the previous verification and the same is being followed during the current verification period. It is to be noted that, due to this deviation, there is no any impact on the applicability of the methodology, additionality or the baseline scenario of the project activity.

3.3 Grouped Projects

Not applicable, as this is not a grouped project activity.

4 DATA AND PARAMETERS

4.1 Data and Parameters Available at Validation

Data / Parameter	EF_{grid,OM,y}
Data unit	tCO ₂ /MWh
Description	Operating Margin CO ₂ emission factor in year y
Source of data	Calculated from CEA database, Version 13, June 2018 ³⁵
Value applied	0.9726
Justification of choice of data or description of measurement methods and procedures applied	Calculated as per "Tool to calculate the emission factor for an electricity system, version 07" as 3-year generation weighted average using data for the years 2014-15, 2015-16 & 2016-17. The data are obtained from "CO ₂ Baseline Database for Indian Power Sector" version 13, published by the Central Electricity Authority, Ministry of Power, Government of India.
Purpose of Data	For the calculation of the baseline emission
Comments	This parameter is fixed ex-ante for the entire crediting period.
Data / Parameter	EF_{grid,BM,y}
Data unit	tCO ₂ /MWh

³⁵https://cea.nic.in/wp-content/uploads/baseline/2020/07/user_guide_ver13.pdf

Description	Build Margin CO ₂ emission factor in year y
Source of data	Calculated from CEA database, Version 13, June 2018 ³⁶
Value applied	0.8723
Justification of choice of data or description of measurement methods and procedures applied	Calculated as per "Tool to calculate the emission factor for an electricity system, version 07" as per the latest data available for the most recent year 2016-17. The data is obtained from "CO ₂ Baseline Database for Indian Power Sector" version 13, published by the Central Electricity Authority, Ministry of Power, Government of India.
Purpose of Data	For the calculation of the Baseline Emission
Comments	This parameter is fixed ex-ante for the entire crediting period.

Data / Parameter	EF_{grid,CM,y}
Data unit	tCO ₂ /MWh
Description	Combined Margin CO ₂ emission factor in year y
Source of data	Calculated from CEA database, Version 13, June 2018 ³⁷
Value applied	0.9475
Justification of choice of data or description of measurement methods and procedures applied	The combined margin emissions factor is calculated as follows: $EF_{grid,CM,y} = EF_{grid,OM,y} * W_{OM} + EF_{grid,BM,y} * W_{BM}$ Where: EF_{grid,BM,y}= Build margin CO₂ emission factor in year y (tCO₂/MWh) EF_{grid,OM,y}= Operating margin CO₂ emission factor in year y (tCO₂/MWh) W_{OM} = Weighting of operating margin emissions factor (%) = 75% W_{BM}= Weighting of build margin emissions factor (%) = 25%
Purpose of Data	For the calculation of the Baseline Emission
Comments	This parameter is fixed ex-ante for the entire crediting period

4.2 Data and Parameters Monitored

For Karnataka Sites

Data / Parameter	EG_{PJ, y,KA}
Data unit	MWh/y
Description	Quantity of net electricity generation supplied by the project plant/unit to the grid in year y in MWh

³⁶https://cea.nic.in/wp-content/uploads/baseline/2020/07/user_guide_ver13.pdf

³⁷https://cea.nic.in/wp-content/uploads/baseline/2020/07/user_guide_ver13.pdf

Source of data	Monthly joint meter reading reports
Description of measurement methods and procedures to be applied	The difference of final value of export and import is used for monthly values of net electricity supplied to the grid by the project activity and same value is considered for ER calculations.
Frequency of monitoring/recording	Continuous measurement & monthly recording
Value monitored	192,765.61 MWh
Monitoring equipment	The electricity exported / supplied by the plant to pooling substation and further to substation. This meter also measures electricity imported by the plant from the grid.
QA/QC procedures to be applied	The meters are approved, tested & sealed by the State Utility. The meters are in the custody of State Utility. The frequency of calibration is once in 5 years. The monthly electricity supplied/exported by the project activity in the JMR report is cross checked with the monthly invoices of sale. In the absence or delay in the meter calibration appropriate Guidelines are applied appropriately to confirm the conservativeness of metering. The metering arrangement, accuracy class of meters, calibration frequency is under control of state electricity board and PP do not have any control on it. PP is getting value of net electricity supplied to grid and the same is considered the monitoring parameter. The meter and meter calibration details are given in Appendix I of Monitoring Report. The billing is raised based on substation meters.
Purpose of the data	Calculation of baseline emissions
Calculation method	Thus, Net electricity supplied to the grid by the project plant in a given month = Export, kWh– Import, kWh. If share certificate/JMR mentioned only net electricity export to grid, and does not mention any export and import separately, then net electricity supplied to grid is considered directly.
Comments	Data archived in paper & electronic form for two years after the end of crediting period or of the last issuance of VERs for this project activity, whichever occurs later.

For Gujarat Site

Data / Parameter	EG_{PJ, y,GJ}
Data unit	MWh/y
Description	Quantity of net electricity generation supplied by the project plant/unit to the grid in year y in MWh

Source of data	Monthly joint meter reading reports
Description of measurement methods and procedures to be applied	The difference of final value of export and import is used for monthly values of net electricity supplied to the grid by the project activity and same value is considered for ER calculations.
Frequency of monitoring/recording	Continuous measurement & monthly recording
Value monitored	22,392.62 MWh
Monitoring equipment	The electricity exported / supplied by the plant to pooling substation and further to substation. This meter also measures electricity imported by the plant from the grid.
QA/QC procedures to be applied	The meters is approved, tested & sealed by the State Utility. The meters are in the custody of State Utility. The frequency of calibration is once in 5 years. The monthly electricity supplied/exported by the project activity in the JMR report is cross checked with the monthly invoices of sale. In the absence or delay in the meter calibration appropriate Guidelines are applied appropriately to confirm the conservativeness of metering. The metering arrangement, accuracy class of meters, calibration frequency is under control of state electricity board and PP do not have any control on it. PP is getting value of net electricity supplied to grid and the same is considered the monitoring parameter. The meter and meter calibration details are given in Appendix I of Monitoring Report. The billing is raised based on substation meters.
Purpose of the data	Calculation of baseline emissions
Calculation method	Thus, Net electricity supplied to the grid by the project plant in a given month = Export, kWh– Import, kWh. If share certificate/JMR mentioned only net electricity export to grid, and does not mention any export and import separately, then net electricity supplied to grid is considered directly.
Comments	Data is archived in paper & electronic form for two years after the end of crediting period or of the last issuance of VERs for this project activity, whichever occurs later.

For Madhya Pradesh Site

Data / Parameter	EG_{PJ, y,MP}
Data unit	MWh/y
Description	Quantity of net electricity generation supplied by the project plant/unit to the grid in year y in MWh

Source of data	Monthly joint meter reading reports
Description of measurement methods and procedures to be applied	The difference of final value of export and import is used for monthly values of net electricity supplied to the grid by the project activity and same value is considered for ER calculations.
Frequency of monitoring/recording	Continuous measurement & monthly recording
Value monitored	28,402.80 MWh
Monitoring equipment	The electricity exported / supplied by the plant to pooling substation and further to substation. This meter also measures electricity imported by the plant from the grid.
QA/QC procedures to be applied	The meters are approved, tested & sealed by the State Utility. The meters are in the custody of State Utility. The frequency of calibration is once in 5 years. The monthly electricity supplied/exported by the project activity in the JMR report is cross checked with the monthly invoices of sale. In the absence or delay in the meter calibration appropriate Guidelines are applied appropriately to confirm the conservativeness of metering. The metering arrangement, accuracy class of meters, calibration frequency is under control of state electricity board and PP do not have any control on it. PP is getting value of net electricity supplied to grid and the same is considered the monitoring parameter. The meter and meter calibration details are given in Appendix I of Monitoring Report. The billing is raised based on substation meters.
Purpose of the data	Calculation of baseline emissions
Calculation method	Thus, Net electricity supplied to the grid by the project plant in a given month = Export, kWh– Import, kWh. If share certificate/JMR mentioned only net electricity export to grid, and does not mention any export and import separately, then net electricity supplied to grid is considered directly.
Comments	Data is archived in paper & electronic form for two years after the end of crediting period or of the last issuance of VERs for this project activity, whichever occurs later.

For Rajasthan Site

Data / Parameter	EG_{PJ, y,RJ}
Data unit	MWh/y
Description	Quantity of net electricity generation supplied by the project plant/unit to the grid in year y in MWh

Source of data	Monthly joint meter reading reports
Description of measurement methods and procedures to be applied	The difference of final value of export and import is used for monthly values of net electricity supplied to the grid by the project activity and same value is considered for ER calculations.
Frequency of monitoring/recording	Continuous measurement & monthly recording
Value monitored	33,387.47 MWh
Monitoring equipment	The electricity exported / supplied by the plant to pooling substation and further to substation. This meter also measures electricity imported by the plant from the grid.
QA/QC procedures to be applied	The meters are approved, tested & sealed by the State Utility. The meters are in the custody of State Utility. The frequency of calibration is once in 5 years. The monthly electricity supplied/exported by the project activity in the JMR report is cross checked with the monthly invoices of sale. In the absence or delay in the meter calibration appropriate Guidelines are applied appropriately to confirm the conservativeness of metering. The metering arrangement, accuracy class of meters, calibration frequency is under control of state electricity board and PP do not have any control on it. PP is getting value of net electricity supplied to grid and the same is considered the monitoring parameter. The meter and meter calibration details are given in Appendix I of Monitoring Report. The billing is raised based on substation meters.
Purpose of the data	Calculation of baseline emissions
Calculation method	Thus, Net electricity supplied to the grid by the project plant in a given month = Export, kWh– Import, kWh. If share certificate/JMR mentioned only net electricity export to grid, and does not mention any export and import separately, then net electricity supplied to grid is considered directly.
Comments	Data is archived in paper & electronic form for two years after the end of crediting period or of the last issuance of VERs for this project activity, whichever occurs later.

For Telangana Site

Data / Parameter	EG_{PJ, y, TL}
Data unit	MWh/y


Description	Quantity of net electricity generation supplied by the project plant/unit to the grid in year y in MWh
Source of data	Monthly joint meter reading reports
Description of measurement methods and procedures to be applied	The difference of final value of export and import is used for monthly values of net electricity supplied to the grid by the project activity and same value is considered for ER calculations.
Frequency of monitoring/recording	Continuous measurement & monthly recording
Value monitored	239,359.52 MWh
Monitoring equipment	The electricity exported / supplied by the plant to pooling substation and further to substation. This meter also measures electricity imported by the plant from the grid.
QA/QC procedures to be applied	The meters are approved, tested & sealed by the State Utility. The meters are in the custody of State Utility. The frequency of calibration is once in 5 years. The monthly electricity supplied/exported by the project activity in the JMR report is cross checked with the monthly invoices of sale. In the absence or delay in the meter calibration appropriate Guidelines are applied appropriately to confirm the conservativeness of metering. The metering arrangement, accuracy class of meters, calibration frequency is under control of state electricity board and PP do not have any control on it. PP is getting value of net electricity supplied to grid and the same is considered the monitoring parameter. The meter and meter calibration details are given in Appendix I of Monitoring Report. The billing is raised based on substation meters.
Purpose of the data	Calculation of baseline emissions
Calculation method	Thus, Net electricity supplied to the grid by the project plant in a given month = Export, kWh– Import, kWh. If share certificate/JMR mentioned only net electricity export to grid, and does not mention any export and import separately, then net electricity supplied to grid is considered directly.
Comments	Data is archived in paper & electronic form for two years after the end of crediting period or of the last issuance of VERs for this project activity, whichever occurs later.

4.3 Monitoring Plan

The monitoring plan is developed in accordance with the modalities and procedures for CDM project activities and is proposed for grid-connected solar

power project being implemented. The monitoring plan, which is implemented by the project participant describes about the monitoring organisation, parameters to be monitored, monitoring practices, quality assurance, quality control procedures, data storage and archiving.

The authority and responsibility for registration, monitoring, measurement, reporting and reviewing of the data rests with the project participant. PP proposed the following structure for data monitoring, collection, data archiving and calibration of equipments for this project activity. The team comprises of the following members:

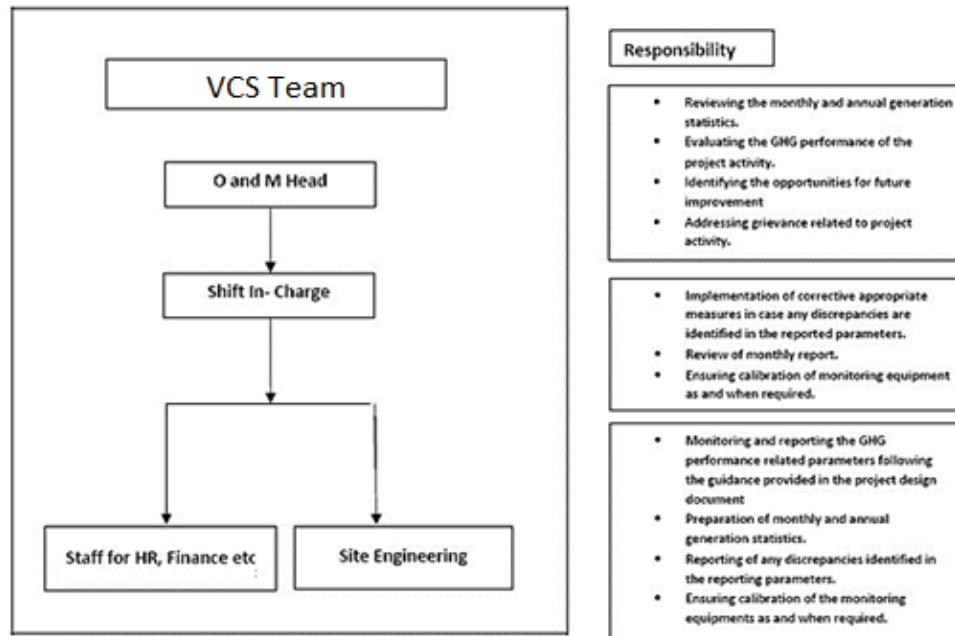

Data Measurement

The export and import energy is measured continuously using above mentioned Main and Check meters located at the substations. Readings of meters are taken on monthly basis by authorized officer of SEB in the presence of PP or representative of PP. Based on the Meter Reading Statement to PP, invoices are raised. These invoices can be used for cross checking the meter readings taken for the respective project activity.

Data collection and archiving

Readings from meters are collected in the presence of the plant in-charge. Export and Import data would be recorded and stored in logs as well as in electronic form on a daily basis. The records are checked periodically by the Plant Manager and discussed thoroughly with the plant supervisor. The period of storage of the monitored data is 2 years after the end of crediting period or till the last issuance of VERs for the project activity whichever occurs later.

Emergency preparedness

The project activity does not result in any unidentified activity that can result in substantial emissions from the project activity. No need for emergency preparedness in data monitoring is visualized.


Personnel training

In order to ensure a proper functioning of the project activity and a properly monitoring of emission reductions, the staff is trained. The plant helpers are trained in equipment operation, data recording, reports writing, operation and maintenance and emergency procedures in compliance with the monitoring plan.

Metering Arrangement


Line diagram with metering arrangement for the solar project activity is shown below.

For Karnataka Site

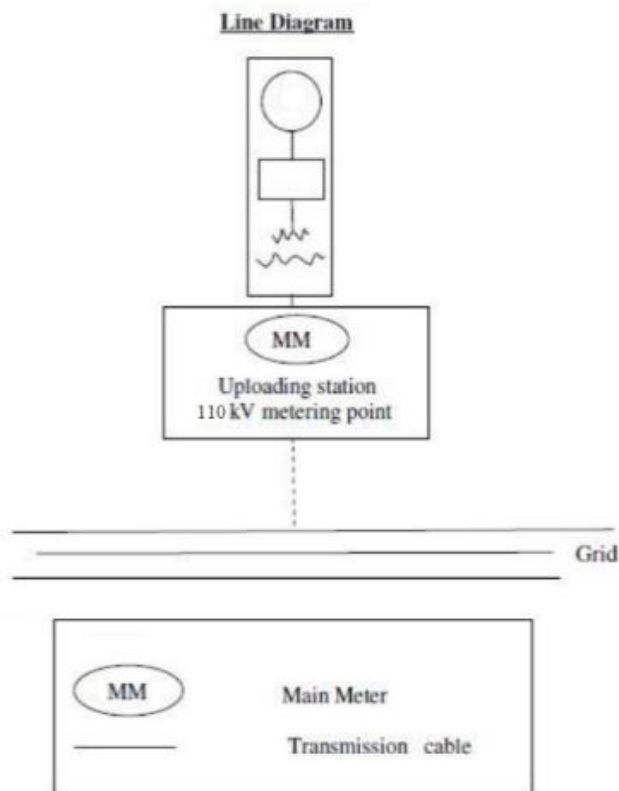


For Rajasthan Site

For Telangana Site

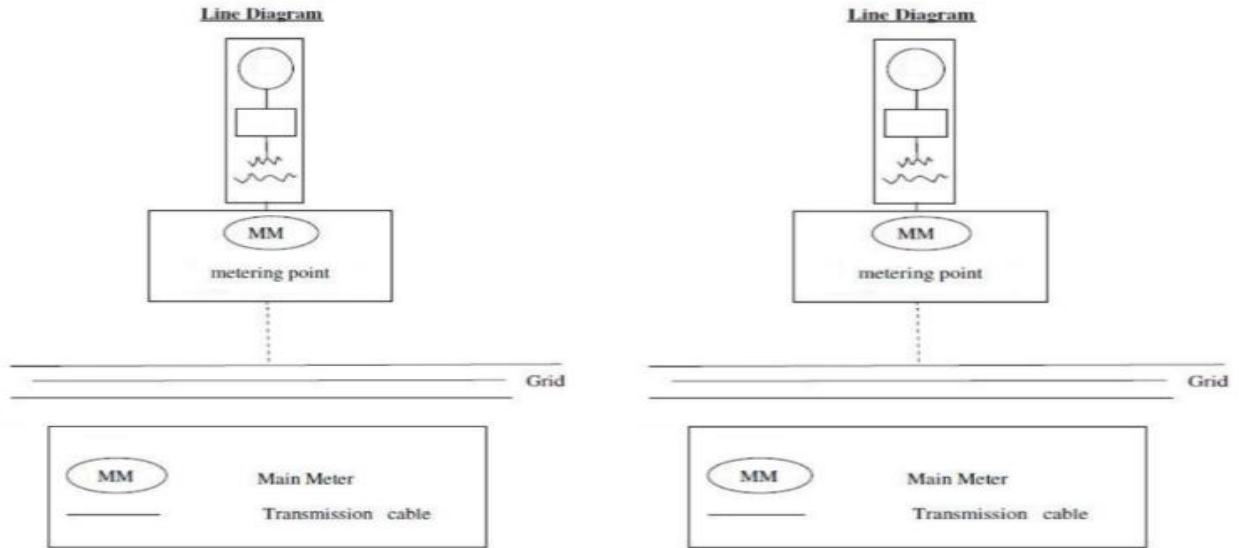

For Madhya Pradesh Site

For Gujarat Site

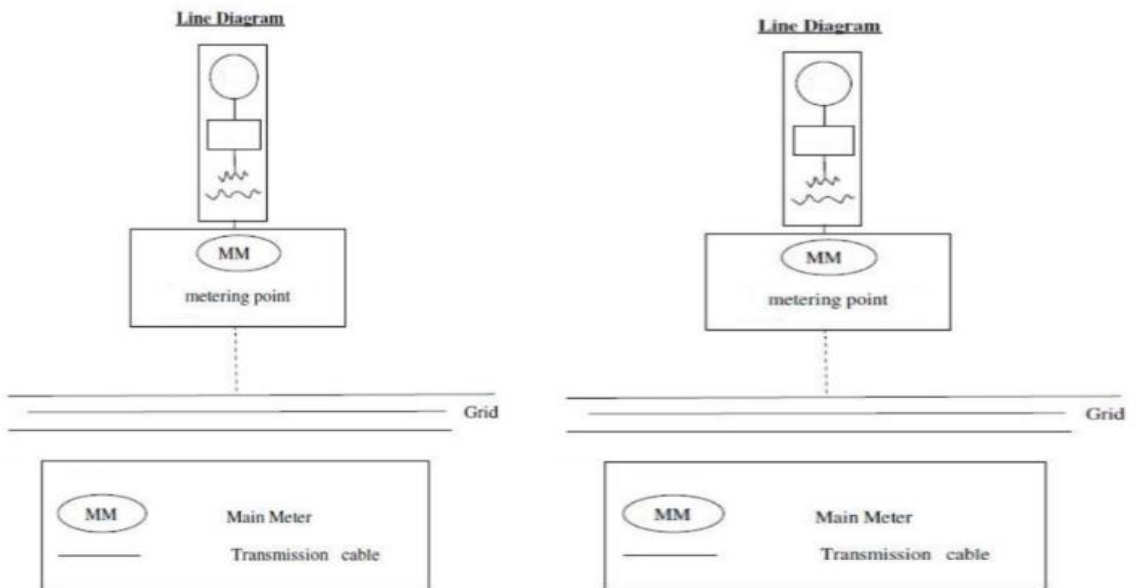

5 QUANTIFICATION OF GHG EMISSION REDUCTIONS AND REMOVALS

5.1 Baseline Emissions

$$BE_y = EG_{PJ,y} * EF_{grid,CM,y}$$

Where:

BE_y : Baseline emissions in year y (tCO₂e/yr)

$EG_{PJ,y}$: Quantity of net electricity generation that is produced and fed into the grid as a result of the implementation of the VCS project activity in year y (MWh/yr)

$EF_{grid,CM,y}$: Combined margin CO₂ emission factor for grid connected power generation in year y calculated using the latest version of the "Tool to calculate the emission factor for an electricity system" (tCO₂e/MWh).

To calculate $EG_{PJ,y}$:

$$EG_{PJ,y} = EG_{PJ,y,KA} + EG_{PJ,y,GJ} + EG_{PJ,y,MP} + EG_{PJ,y,RJ} + EG_{PJ,y,TL}$$

For Karnataka Sites:

$EG_{PJ,y,KA}$: Quantity of net electricity generation supplied by the project plant/unit to the grid in year y in MWh (For the Karnataka site)

The net electricity supplied to the grid is calculated as the difference between the total electricity supplied to the grid and 115% of the total electricity imported from the grid i.e.

$$EG_{PJ,y,KA} = \text{Export (MWh)} - 115\% * \text{Import (MWh)} \text{ (Where applicable)} = 192,765.61 \text{ MWh}$$

For Gujarat sites:

$EG_{PJ,y,GJ}$: Quantity of net electricity generation supplied by the project plant/unit to the grid in year y in MWh (For the Gujarat site)

The net electricity supplied to the grid is calculated as the difference between the total electricity supplied to the grid and total electricity imported from the grid i.e.

$$EG_{PJ,y,GJ} = \text{Export (MWh)} - \text{Import (MWh)} = 22,392.62 \text{ MWh}$$

For Madhya Pradesh Sites:

$EG_{PJ,y,MP}$: Quantity of net electricity generation supplied by the project plant/unit to the grid in year y in MWh (For the Madhya Pradesh site)

The net electricity supplied to the grid is calculated as the difference between the total electricity supplied to the grid and total electricity imported from the grid i.e.

$$EG_{PJ,y,MP} = \text{Export (MWh)} - \text{Import (MWh)} = 28,402.80 \text{ MWh}$$

For Rajasthan Sites:

$EG_{PJ,y,RJ}$: Quantity of net electricity generation supplied by the project plant/unit to the grid in year y in MWh (For the Rajasthan site)

The net electricity supplied to the grid is calculated as the difference between the total electricity supplied to the grid and total electricity imported from the grid i.e.

$$EG_{PJ,y,MP} = \text{Export (MWh)} - \text{Import (MWh)} = 33,387.47 \text{ MWh}$$

For Telangana Sites:

$EG_{PJ,y,TL}$: Quantity of net electricity generation supplied by the project plant/unit to the grid in year y in MWh (For the Telangana site)

The net electricity supplied to the grid is calculated as the difference between the total electricity supplied to the grid and total electricity imported from the grid i.e.

$$EG_{PJ,y,TL} = \text{Export} - \text{Import (MWh)} = 239,359.52 \text{ MWh}$$

Hence:

$$EG_{PJ,y} = 192,765.61 + 22,392.62 + 28,402.80 + 33,387.47 + 239,359.52$$

$$EG_{PJ,y} = 516,308.01 \text{ MWh}$$

Total Baseline emission for the Monitoring period:

Parameter	Unit	Value
$EG_{PJ,y}$	MWh	516,308.01
$EF_{grid,CM,y}$	tCO ₂ e/MWh	0.9475
BE_y	tCO ₂ e	$516,308.01 * 0.9475$
	=	489,201 (Round down)

$$BE_y = 489,201 \text{ tCO}_2\text{e (Round down value)}$$

5.2 Project Emissions

Not applicable, since project emissions from the solar project activity is zero as per ACM0002 methodology. Hence, $PE_y = 0$.

5.3 Leakage

Not applicable, since leakage emissions from the solar project activity is zero as per ACM0002 methodology. Hence, $LE_y = 0$.

5.4 Net GHG Emission Reductions and Removals

Emission Reductions are calculated as follows:

$$ER_y = BE_y - PE_y$$

Where:

ER_y = Emission reductions in the year y (tCO₂e/yr)

BE_y = Baseline emissions in the year (tCO₂e/yr)

PE_y = Project emissions in the year y (tCO₂e/yr)

Baseline emissions:

$$BE_y = EG_{PJ,y} * EF_{grid,CM,y}$$

Where:

BE_y : Baseline emissions in year y (tCO₂e/yr)

$EG_{PJ,y}$: Quantity of net electricity generation that is produced and fed into the grid as a result of the implementation of the VCS project activity in year y (MWh/yr)

$EF_{grid,CM,y}$: Combined margin CO₂ emission factor for grid connected power generation in year y calculated using the latest version of the "Tool to calculate the emission factor for an electricity system" (tCO₂e/MWh).

$$BE_y = 516,308.01 \text{ MWh} * 0.9475 \text{ tCO}_2\text{e/MWh}$$

$$BE_y = 489,201 \text{ tCO}_2\text{e (Round down)}$$

As per the ACM0002 methodology, Project emissions (PE_y) are Zero.

Hence,

$$ER_y = BE_y - PE_y$$

$$ER_y = 489,201 \text{ tCO}_2\text{e (Round down)}$$

Year	Baseline emissions or removals (tCO ₂ e)	Project emissions or removals (tCO ₂ e)	Leakage emissions (tCO ₂ e)	Net GHG emission reductions or removals (tCO ₂ e)
01-January-2023 to 31-March-2023	489,201	0	0	489,201
Total	489,201	0	0	489,201

<u>Ex-ante emissions reductions/removals</u>	<u>Achieved emissions reductions/removals</u>	<u>Percent difference</u>	<u>Justification for the difference</u>
435,768	489,201	12.26%	It is to be noted here that as per the estimated emission reduction to be achieved from the project activity for the current monitoring period is 435,768 tCO ₂ e, whereas actual

		emission reductions achieved are 489,201 tCO₂e, which is approximately 12.26% higher than the estimated emission reductions. The generation of electricity depends upon many other climatic conditions, which are not within the control of the project participant. The higher generation during the current verification period is due to certain natural conditions and it doesn't breach the additionality of the project. Hence, it is acceptable.
--	--	---

APPENDIX I: <METER CALIBRATION DETAILS>

S. No.	SPV Name	Location	Meter Number	Meter Type	Meter Manufacturer	Meter Accuracy Class	Date of Calibration	Due date of calibration
1	Tarun Kiran Bhoomi Private Limited (20 MW)	Alland	16193095	Main Meter	L & T	0.2 s	04-September-2019, 19-June-2020	03-September-2024, 18-June-2025
			21004943 ³⁸	Main Meter	L&T	0.2s	05-April-2022	04-April-2027
			13192165	Check Meter	L & T	0.2 s	04-September-2019, 19-June-2020	03-September-2024, 18-June-2025
			21005013	Check Meter	L&T	0.2s	05-April-2022	04-April-2027
2	Renew Clean Energy Private Limited (51 MW)	Ashokenagar	XE518730	Main Meter	Secure	0.2 s	10-August-2020	09-August-2025
			XE518731	Check Meter	Secure			
			Q0715876	Main Meter	Secure	0.2s	01-March-2023	29-Feb-2028
			Q0715877	Check Meter	Secure	0.2s	01-March-2023	
3	Renew Wind Energy (TN2) Private Limited (50 MW)	Tumkur	16195517	Main Meter	L & T	0.2 s	08-December-2017	07-December-2022
			16195508	Check Meter	L & T	0.2 s	08-December-2017	
			16195519	Main Meter	L & T	0.2 s	08-December-2017	
			16195523	Check Meter	L & T	0.2 s	08-December-2017	
			LT-0834-A	Main Meter	L & T	0.2 s	10-January-2022	09-January-2027
			LT-0795-A	Check Meter	L & T	0.2 s	10-January-2022	

³⁸ Meter No. 16193095 & 13192165 were replaced by new meter no. 21004943 & 21005013 respectively on 05/04/2022.

			LT-0921-A	Main Meter	L & T	0.2 s	10-January-2022	
			LT-0922-A	Check Meter	L & T	0.2 s	10-January-2022	
4	Renew Wind Energy (Karnataka 3) Private Limited (20 MW)	Bhalki	16113413	Main Meter	L & T	0.2 s	28-January-2021	27-January-2026
			16113221	Check Meter	L & T	0.2 s	28-January-2021	
			21005034	Main meter	L & T	0.2 s	15-March-2023	14-March-2028
			21005051	Check Meter	L & T	0.2 s		
5	Renew Wind Energy (MP Four) Private Limited (20 MW)	Chincholi	16083161	Main Meter	L & T	0.2 s	10-June-2021	09-June-2026
			16083118	Check Meter	L & T	0.2 s	10-June-2021	
6	Bhumi Prakash Private Limited (20 MW)	Devadurga	15197833	Main Meter	L & T	0.2 s	25-December-2019	24-December-2024
			15197834	Check Meter	L & T	0.2 s	25-December-2019	
			21005057	Main Meter	L & T	0.2 s	24-February-2023	23-February-2028
			21005109	Check Meter	L & T	0.2 s	24-February-2023	
7	ReNew Solar Energy (Telangana) Private Limited (143 MW)	Dichpally	APX01166	Main Meter	Secure	0.2 s	27-July-2021	26-July-2026
			APX01167	Check Meter	Secure	0.2 s	27-July-2021	
			APX01168	Stand by Meter	Secure	0.2 s	27-July-2021	
8	Renew Wind Energy (MP Three) Private Limited (20 MW)	Honnali	16112933	Main Meter	L & T	0.2 s	27-September-2017	26-September-2022
			16112921	Check Meter	L & T	0.2 s	27-September-2017	
			21005015	Main Meter	L & T	0.2 s	21-January-2023	20-January-2028

			21005085	Check Meter	L & T	0.2 s	21-January-2023	
9	Renew Wind Energy (Karnataka 4) Private Limited(20 MW)	Humnabad	16083139	Main Meter	L & T	0.2 s	11-February-2021	10-February-2026
			16083133	Check Meter	L & T	0.2 s	11-February-2021	
10	Renew Mega Solar Power Pvt Limited (48 MW)	Mandamarri	APX01147	Main Meter	Secure	0.2 s	10-July-2020	09-July-2025
			APX01148	Check Meter	Secure	0.2 s	10-July-2020	
			APX01149	Stand by Meter	Secure	0.2 s	10-July-2020	
11	Renew Wind Energy (TN2) Private Limited (100 MW)	Mahbubnagar	APZ00378	Main Meter	Apex 150	0.2 s	15-June-2022	14-June-2023
			APZ00379	Check Meter	Apex 150	0.2 s	15-June-2022	
			APZ00380	Stand by Meter	Apex 150	0.2 s	15-June-2022	
12	Renew Saur Shakti Private Limited (65 MW)	Minpur	16196322	Main Meter	L & T	0.2 s	18-February-2020	17-February-2025
			16196377	Check Meter	L & T	0.2 s	18-February-2020	
			16196411	Stand by Meter	L & T	0.2 s	18-February-2020	
13	Renew Saur Shakti Private Limited (30 MW)	Mulkanoor	16196362	Main Meter	L & T	0.2 s	09-February-2021	08-February-2026
			16196398	Check Meter	L & T	0.2 s	09-February-2021	
			16196385	Stand by Meter	L & T	0.2 s	09-February-2021	
14	Abha Solarfarms Limited (10 MW)	Bap	17075486	Main Meter	L & T	0.2 s	03-April-2021	02-April-2026
			17075488	Check Meter	L&T	0.2s	03-April-2021	02-April-2026
15	Aalok Solarfarms Limited (10 MW)	Bap	17075514	Main Meter	L & T	0.2 s	03-April-2021	02-April-2026
			17075515	Check Meter	L&T	0.2s	03-April-2021	02-April-2026

16	Heramba Renewables Limited (20 MW)	Bap	17075537	Main Meter (Project-I)	L & T	0.2 s	05-April-2021	04-April-2026
			17075539	Check Meter (Project-I)	L & T	0.2 s	05-April-2021	
			17075547	Main Meter (Project-II)	L & T	0.2 s	05-April-2021	
			17075548	Check Meter (Project-II)	L & T	0.2 s	05-April-2021	
17	Shreyas Solarfarms Limited (20 MW)	Bap	17075525	Main Meter (Project-I)	L & T	0.2 s	04-April-2021	03-April-2026
			17075526	Check Meter (Project-I)	L & T	0.2 s	04-April-2021	
			17075530	Main Meter (Project-II)	L & T	0.2 s	04-April-2021	
			17075531	Check Meter (Project-II)	L & T	0.2 s	04-April-2021	
18	Prathamesh Solarfarms Limited (50 MW)	Dodaguntapally	XD551233	Main Meter	Secure	0.2 s	25-March-2021	24-March-2026
			XD551234	Check Meter	Secure	0.2 s	25-March-2021	
			XD551235	Stand by Meter	Secure	0.2 s	25-March-2021	
19	Renew Solar Energy (Karnataka Two) Private Limited (40 MW)	Charanka	GJ3713A	Main Meter	Secure	0.2 s	19-March-2020	18-March-2025
			GJ3714A	Check Meter	Secure	0.2s	19-March-2020	18-March-2025
			GJ3880A	Stand by Meter	Secure	0.2 s	19-March-2020	18-March-2025
20	Renew Wind Energy	Turuvekere	16112918	Main Meter	L & T	0.2 s	26-February-2021	25-February-2026

	(Rajasthan Four) Private Limited (20 MW)		16112913	Check Meter	L & T	0.2 s	26-February-2021	30-January-2028
			20009661	Main Meter	L & T	0.2 s	31-January-2023	
			20009673	Check Meter	L & T	0.2 s	31-January-2023	
21	Renew Wind Energy (Maharashtra) Private Limited (20 MW)	Yadgir	16113430	Main Meter	L & T	0.2 s	01-April-2021	31-March-2026
			16113436	Check Meter	L & T	0.2 s	01-April-2021	
			21004929	Main Meter	L & T	0.2 s	01-March-2023	29-Feb-2028
			21004938	Check Meter	L & T	0.2 s		
22	Renew Agni Power Private Limited (20 MW)	Siruguppa	16113386	Main Meter	L & T	0.2 s	13-January-2021	12-January-2026
			16113401	Check Meter	L & T	0.2 s	13-January-2021	
			20003009	Main Meter	L & T	0.2 s	16-March-2023	15-March-2028
			20003005	Check Meter	L & T	0.2 s	16-March-2023	
23	Renew Wind Energy (Budh 3) Private Limited (20 MW)	Eklara	17069178	Main Meter	L & T	0.2 s	26-November-2020	25-November-2025
			17069183	Check Meter	L & T	0.2 s	26-November-2020	
			21004949	Main Meter	L&T	0.2 s	14-March-2023	13-March-2028
			21004979	Check Meter	L&T	0.2 s	14-March-2023	
24	Renew Saur Urja Private Limited (50 MW)	Thalekan	17117926	Main Meter	L & T	0.2 s	25-February-2021	24-February-2026
			17117928	Check Meter	L & T	0.2 s	25-February-2021	
25	Renew Wind Energy (Budh 3) Private Limited (20 MW)	Nirna	17166928	Main Meter	L & T	0.2 s	12-June-2020	11-June-2025
			17166940	Check Meter	L & T	0.2 s	12-June-2020	
			21005004	Main Meter	L & T	0.2 s	13-March-2023	12-March-2028
			21005028	Check Meter	L & T	0.2 s	13-March-2023	

26	Renew Wind Energy (Budh 3) Private Limited (20 MW)	Wadagere	1712558 9	Main Meter	L & T	0.2 s	01-April- 2021	31-March- 2026
			1712559 0	Check Meter	L & T	0.2 s	01-April- 2021	31-March- 2026
			1712558 9	Main Meter	L & T	0.2 s	16-Feb- 2023	15-Feb- 2028
			1712559 0	Check Meter	L & T	0.2 s	16-Feb- 2023	
